Sprint Report #9

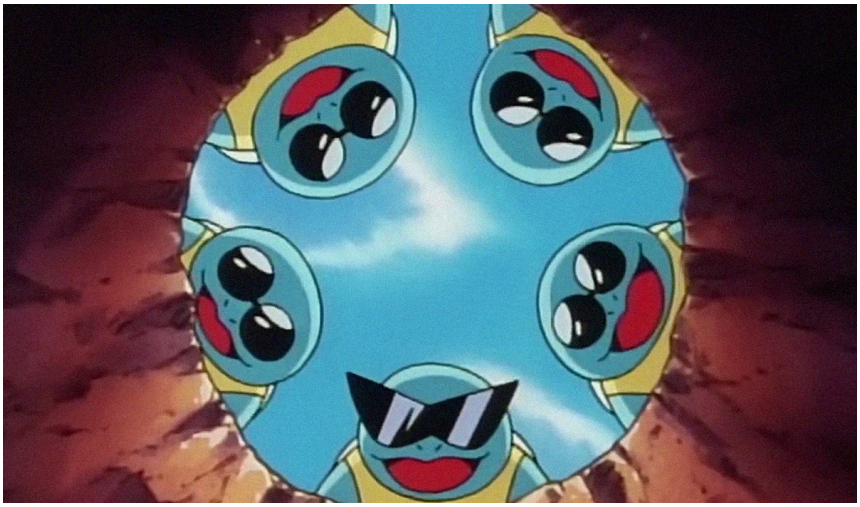

Roles

Scrum Master: Kaylee Harold
Product Owner: Johnny Yang
Developers: Melanie Magno, Jorge Nunez, Aurora Liles

Expectations

This sprint was focused on midterm 2 deliverables and finishing up automated testing. We wanted to add the final features we had planned, but we are having to pivot to security and server hosting. The plan is to research, and see if it is feasible to implement this within the last sprint.

Executions - what we did

Melanie: Updated database file and fixed recurring back end issues. Finished add transaction page. Also helped with ensuring documentation was in file for the midterm 2 submission.

Aurora: Completed remaining midterm 2 documents and assisted with integration efforts.

Johnny: Working on the pie chat, made many improvements to the home page and the Logout button, fix codes from recent merge.

Kaylee: Worked on automated testing of the User and Categories routes using github actions, as well as help Jorge script transactions.

Jorge: Worked on automated testing for Transactions routed using github actions.

Task	Owner	Status	Planned hrs.	Actual hrs.	Challenges/Solutions
Finished editing page logic-removed unnecessary code	Melanie	completed	4	4	None this week. Mostly just making sure my code was implemented into the main branch so we could present it to the teacher on Tuesday. Also, helped ensure documentation was up to date on repo for midterm 2.
Automated Testing	Kaylee	Complete	4	4	Helping Jorge script his tests, as well as debug everything that has come up with our own.
Midterm documentation	Aurora	Completed	4	3	Trying to document the continuous changes introduced by the professor and support the team in adapting.
Automated Testing	Jorge	Complete	4	4	Created automated tests for Transactions and debugged issues.
Pie Chart	Johnny	ongoing	4	5	Continue working on the pie chart and fixing code from a recent merge.

User Stories Worked/In Progress

Worked:

- As a user, I want to be able to enter my spent and earned money, so that I can keep track of how much money I have in a certain time period.
- As a user, I want to be able to view my net earnings calculated automatically by the app, so that I have to do as little math as possible.
- As a user, I want to be able to enter my spent and earned money, so that I can keep track of how much money I have in a certain time period.
- As a graduating student that wants to budget for the future in order to save to purchase a house, I want to be able to log my biweekly paychecks as well as my monthly planning in order to estimate how much money I need to save per month.
- As an individual who owns my own home (IN THIS ECONOMY??), so I want to be able to logout so no homeless person can log into my account.
- As an incompetent individual, I want to be able to visualize my whole income to see where my bills are going towards (like a piechart or something that shows how much of my income has been utilized).

In Progress:

- None.

Pros of team

At this point, the team is over this project, and is working extra hours to get the final product on the table.

Cons of team

The team has been working to debug some unexpected things that went wrong with the database, and had to pause what they were doing to debug what broke. The communication between the four have been great, but there is still a lack of communication with one team member.

Sprint Retrospective

Start – Stop – Continue
Start: finalizing the project.
Stop: Adding new features.
Continue: Scripting tests.

Concerns - Discussion & Resolution

Sprint Review

Daily Scrum 4-14

Today was the Midterm 2, so we spent most of the time working on the deliverables needed. We are still doing testing for Budget routes, but the rest of it is complete. Johnny is still working on the same stuff he started at the end of the semester. They are finishing up implementing and testing the front end,and we plan to do a final walkthrough next week.

Daily Scrum 4-16

Most of us were out at today, however we are trying to research the security and server hosting for the last sprint. It's honestly not feasible, and if we knew ahead of time it would need to be hosted, then we could've planned for that.

Time worked per employee (unpaid interns):

Kaylee - 4 hours on midterm documentation and sprint report.
Aurora - 3 hours working on midterm documentation.
Jorge - 4 hours working on automated tests.
Johnny - worked on the pie chart 4 hours, 1 hour resolving merge conflicts.
Melanie - ensure documentation was up to date on repo for midterm 2.

Roles for next sprint

Scrum Master: Johnny Yang

Product Owner: Melanie Magno

Product Owner Summary (Johnny)

Sprint Goal

Our goal for sprint 9 was mostly to finish up debugging and final implementations, as well as start on automated testing with github actions. We are merging codes and getting the bugs out of it. The pie chart needs to be refined. The website looks more consistent now, and refined css styling to make the site accessible.

Completed Stories

- As an incompetent individual, I want to be able to visualize my whole income to see where my bills are going towards (like a pie chart or something that shows how much of my income has been utilized).

Business Value

- Improved accessibility across the site with visible text and theme.
- Improved site stability with hotfixes and debugging
- Updated design language from default. Improved usability.

Acceptance Criteria and Results

- Continual hotfixes and debugging - As necessary
- Product accessible to all users. - Met

Next Sprint Goal

- Finalize UI.
- Finalize integration of backend
- Finalize Front end
